


Sprint Review Form

Group:	4
Sprint:	1
Members:	Matthew Sherwood (22034915), Reece Turner (22036698), Levente Mate (22037146), Ksawery Buczek (22031584), Kane Hill (22038385).

1.0 Burndown Charts

1.1 Setting up the project

Date - 27 January 2025 - 16 February 2025

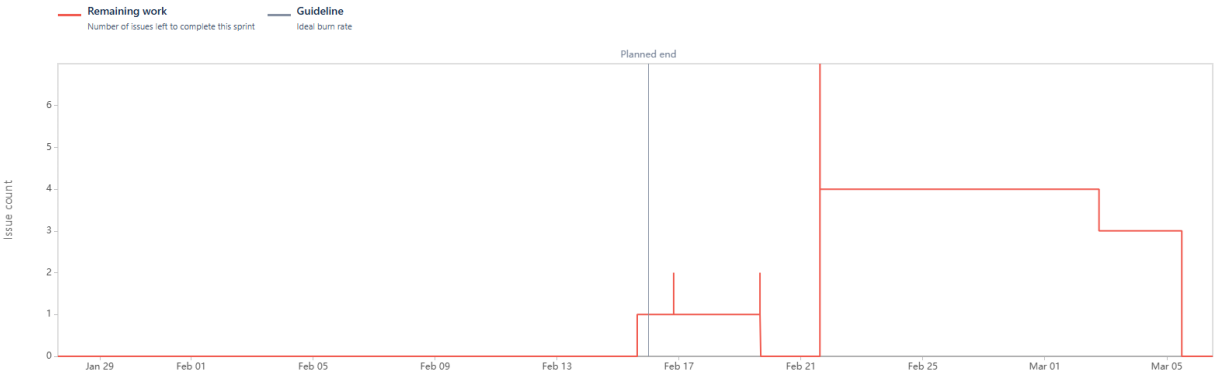

Report: Sprint 0 - Setup

*Issue added after sprint start

Scope changes log

[View in issue navigator](#)


Date	Key	Summary	Issue type	Epic	Details of scope change	Change in estimation
2025-02-15	DS-15*	Create Database Diagram	Task	SPRINT 1	Issue added to sprint	1
2025-02-16	DS-59*	Create docker compose	Task	SPRINT 0	Issue added to sprint	1
2025-02-19	DS-61*	Create Postgres Databases from Diagram	Task	SPRINT 1	Issue added to sprint	1
2025-02-19	DS-15	Create Database Diagram	Task	SPRINT 1	Issue removed from sprint	-1
2025-02-19	DS-61	Create Postgres Databases from Diagram	Task	SPRINT 1	Issue removed from sprint	-1
2025-02-21	DS-59	Create docker compose	Task	SPRINT 0	Issue removed from sprint	-1
2025-02-21	DS-88*	Setup GitHub repository	Task		Issue added to sprint	1
2025-02-21	DS-89*	Create Codebase structure	Task		Issue added to sprint	1
2025-02-21	DS-90*	Define roles for group members	Task		Issue added to sprint	1
2025-02-21	DS-91*	Setup Jira with task assignments	Task		Issue added to sprint	1
2025-02-21	DS-92*	Define sprint goals	Task		Issue added to sprint	1
2025-02-21	DS-93*	Assign story points to tasks	Task		Issue added to sprint	1
2025-02-21	DS-94*	Assign tasks to group members	Task		Issue added to sprint	1
2025-02-21	DS-59*	Create docker compose	Task	SPRINT 0	Issue added to sprint	1

UFCFTR-30-3

Distribute & Enterprise Software Development

We had an issue on Jira where our completed tasks would vanish from the backlog preventing us from viewing them. However, Sprint 0 is part of Sprint 1 as a pre-requisite to ensure optimal configurations are in place for the foreseeable future of the project.

1.2 Backend

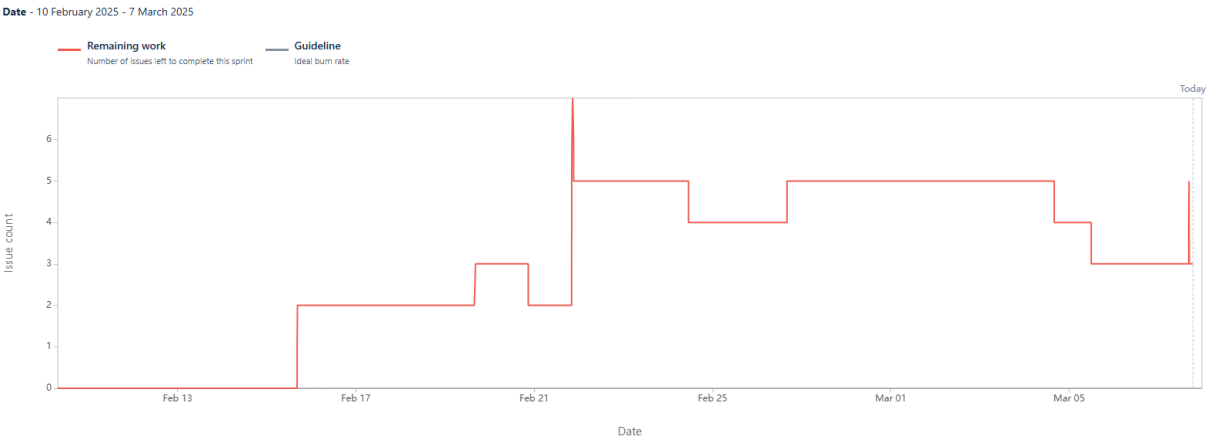

Report: Sprint 1 - Backend

*Issue added after sprint start

Scope changes log

[View in issue navigator](#)


Date	Key	Summary	Issue type	Epic	Details of scope change	Change in estimation
2025-02-15	DS-40*	Backend - Create Docker Compose	Task	SPRINT 1	Issue added to sprint	1
2025-02-15	DS-48*	Backend - Design Database	Task	SPRINT 1	Issue added to sprint	1
2025-02-19	DS-15*	Create Database Diagram	Task	SPRINT 1	Issue added to sprint	1
2025-02-19	DS-61*	Create Postgres Databases from Diagram	Task	SPRINT 1	Issue added to sprint	1
2025-02-21	DS-107*	Backend - Database scheme and SQL	Task	SPRINT 1	Issue added to sprint	1
2025-02-21	DS-110*	Backend - User Login	Task	SPRINT 1	Issue added to sprint	1
2025-02-21	DS-111*	Backend - User Registration	Task	SPRINT 1	Issue added to sprint	1
2025-02-21	DS-118*	Backend - User Authentication System	Task	SPRINT 1	Issue added to sprint	1
2025-02-21	DS-127*	Backend - Dashboard API Endpoints	Task	SPRINT 1	Issue added to sprint	1
2025-02-26	DS-172*	Backend - Managing Accounts	Task	SPRINT 1	Issue added to sprint	1
2025-03-07	DS-15	Create Database Diagram	Task	SPRINT 1	Issue removed from sprint	-1
2025-03-07	DS-61	Create Postgres Databases from Diagram	Task	SPRINT 1	Issue removed from sprint	-1
2025-03-07	DS-61*	Create Postgres Databases from Diagram	Task	SPRINT 1	Issue added to sprint	1
2025-03-07	DS-15*	Create Database Diagram	Task	SPRINT 1	Issue added to sprint	1
2025-03-07	DS-64*	Frontend - User Dashboard	Task	SPRINT 1	Issue added to sprint	1
2025-03-07	DS-64	Frontend - User Dashboard	Task	SPRINT 1	Issue removed from sprint	-1

UFCFTR-30-3

Distribute & Enterprise Software Development

1.3 Frontend

Date - 10 February 2025 - 7 March 2025

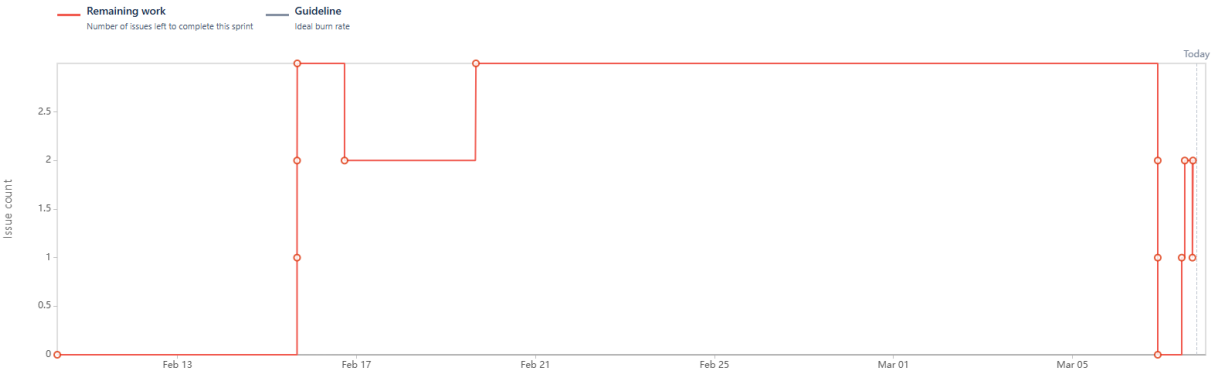

The reason for the burndown on the frontend being so high is due to the restructuring of more recent issues, specifically those of dashboards being moved from the next sprint to this sprint as we felt there was not much to complete for the user interface at this current time. Doing so would be beneficial for the next sprint as the completion stages are much larger.

Report: Sprint 1 - Frontend

*Issue added after sprint start

Scope changes log

[View in issue navigator](#)

Date	Key	Summary	Issue type	Epic	Details of scope change	Change in estimation
2025-02-15	DS-32*	Frontend - Implement role-aware header & static footer component.	Task	SPRINT 1	Issue added to sprint	1
2025-02-15	DS-34*	Frontend - Create and style the index page.	Task	SPRINT 1	Issue added to sprint	1
2025-02-15	DS-38*	Frontend - Implement static login & registration forms.	Task	SPRINT 1	Issue added to sprint	1
2025-02-16	DS-34	Frontend - Create and style the index page.	Task	SPRINT 1	Issue removed from sprint	-1
2025-02-19	DS-34*	Frontend - Create and style the index page.	Task	SPRINT 1	Issue added to sprint	1
2025-02-21	DS-59*	Create docker compose	Task	SPRINT 0	Issue added to sprint	1
2025-02-21	DS-59	Create docker compose	Task	SPRINT 0	Issue removed from sprint	-1
2025-03-07	DS-64*	Frontend - User Dashboard	Task	SPRINT 1	Issue added to sprint	1
2025-03-07	DS-15*	Create Database Diagram	Task	SPRINT 1	Issue added to sprint	1
2025-03-07	DS-61*	Create Postgres Databases from Diagram	Task	SPRINT 1	Issue added to sprint	1
2025-03-07	DS-61	Create Postgres Databases from Diagram	Task	SPRINT 1	Issue removed from sprint	-1
2025-03-07	DS-15	Create Database Diagram	Task	SPRINT 1	Issue removed from sprint	-1
2025-03-07	DS-76*	Frontend - Admin Dashboard	Task	SPRINT 1	Issue added to sprint	1
2025-03-07	DS-64	Frontend - User Dashboard	Task	SPRINT 1	Issue removed from sprint	-1
2025-03-07	DS-64*	Frontend - User Dashboard	Task	SPRINT 1	Issue added to sprint	1

2.0 Backlog

Projects / Distributed Project1

All sprints

Q Search

RT

LM

KH

KB

Epic 1

Sprint 2

Clear filters

TO DO 2 OF 2

IN PROGRESS 3 OF 3

DONE 10 OF 10

RT

Reece Turner (4 issues)

+ Create issue

Frontend - Admin Dashboard

SPRINT 1 07 MAR

DS-76

10

RT

Create Database Diagram

SPRINT 1 18 FEB

DS-45

7

RT

Create Postgres Databases from Diagram

SPRINT 1 19 FEB

DS-61

8

RT

Backend - Design Database

SPRINT 1 26 FEB

DS-48

12

RT

UFCFTR-30-3

Distribute & Enterprise Software Development

▼  Kane Hill (4 issues)

+ Create issue

Backend - Database scheme and SQL

SPRINT 1 26 FEB

✓ DS-107 5    KH

Backend - Create Docker Compose

SPRINT 1 28 FEB

✓ DS-40 18    KH

Backend - User Login

SPRINT 1 04 MAR

✓ DS-110 5    KH

Backend - User Registration

SPRINT 1 05 MAR

✓ DS-111 6    KH

▼  Ksawery Buczek (2 issues)

Backend - Managing Accounts

SPRINT 1 14 MAR

✓ DS-172 13   KB

+ Create issue

Backend - User Authentication System

SPRINT 1 10 MAR

✓ DS-118 12    KB

UFCFTR-30-3

Distribute & Enterprise Software Development

▼  Levente Mate (4 issues)

+ Create issue

Frontend - User Dashboard

SPRINT 1

07 MAR

✓ DS-64

7



LM

Frontend - Implement role-aware header & static footer component.

SPRINT 1

05 MAR

✓ DS-32

✓

5



LM

Frontend - Implement static login & registration forms.

SPRINT 1

05 MAR

✓ DS-38

✓

1



LM

Frontend - Create and style the index page.

SPRINT 1

06 MAR

✓ DS-34

✓

2



LM

▼ Unassigned (1 issue)

Backend - Dashboard API Endpoints

SPRINT 1

14 MAR

✓ DS-127

15



+ Create issue

3.0 Communication Issues

During the initial start-up and first sprint, we faced significant communication issues that hindered our progress. This occurred due to being in a group that had not previously worked together, which caused delayed responses to essential questions and slowed down progress, as members were left unanswered. Moreover, our misaligned time constraints meant flexibility was dwindling therefore our communication skills needed to be sorted with haste which was partially reinstated by invoking a Microsoft Team's meeting at 12-1pm on 15/02/2025.

However, we weren't primarily using teams as our communication was also coupled with another vocal median Discord. Our group felt it provided more value to us as you are more likely to get notified about a message prompting the assistance of an individual. Conversely, this became a major concern when adhering to professional frameworks due to our group chat burying previous issues when a new individual comments, which led to them not being acknowledged and therefore not getting the attention needed. In hindsight, this could've been sorted through a server-based group rather than a group chat, but the group refused to change platforms.

4.0 Reflections

Concerning sprint one, our efforts have been pre-emptively established in the organisation by first establishing roles:

- Kane: Back-End, and Management.
- Levente: Front-End and Design.
- Reece: Front-End, Database Admin, and Project Manager.
- Ksawery: Backend and Security.
- Matt: Backend and Communications.

Next, Reece - as the Project Manager - liaised with Kane with the initial folder structure to address project requirements. From there we realised the docker environment could not be configured without the PostgreSQL databases, so Reece spent the day normalising the data to be suitable for 3rd Normal Form while Kane set up the Django and Docker requirements. Additionally, we delineated other role-related requirements with the rest of the team by providing them with simple tasks to understand the frameworks and codebases in the beginning. This was beneficial for ensuring our project's result is concrete and robust.

Next, Kane developed the login and registration system, and we're pleased with its functionality, as it passed testing successfully. This provided a solid foundation for building our role system. We prioritised security by implementing third-party services and proper handling techniques. We use cookies only for non-sensitive preferential data to minimise security risks, and authentication tokens (JWTs) are stored in HttpOnly cookies to mitigate XSS threats. Additionally, phone verification is managed through Twilio, and temporary data is cached to ensure sensitive details are only stored after successful verification.

Leventes' work has made up our core design philosophy regarding the presentation of our website. Contributing greatly towards the development of our index page, both in its headers and footers, but also its login and registration forms alongside its crisp functionality. We collaboratively felt a white and blue colour scheme assisted our health theme due to NHS denotations, however, Levente handled much of implementing the styling. Even going to the lengths of creating our registration icons from scratch.

We aimed to go beyond the sprint one's criteria in terms of content, having done so Ksawery has begun work on core backend functionality such as the user authentication system; ensuring we've considered every possibility as relates to our use-case and as concerns security exploits. Additionally, implementing our account management which plays a vital role in our website's functionality, again reiterates the theme of security confirming sensitive data isn't at risk, and exploits are evaded.

The services, i.e. functionality, is handled via API endpoints which Matt has begun developing. Critical components that adhere to the primary OOP principle such as encapsulation, provide the modularity necessary to avoid the website interacting directly with our database or otherwise business logic. The contents of these endpoints will make or break both the functionality and reliability of our website.

Lastly, throughout our short collaboration, we've been actively improving our communication. Initially had difficulty due to the short face-to-face time at university, and prominent time working with troublesome applications like Microsoft Teams. We opted to move to Discord to improve our efficiency, while better it wasn't ideal, however, we've recently used Discord's server functionality and since then feel we're set up greatly to exceed our expectations.

While we didn't meet our initial goals, which would have put us two weeks ahead of the project timeline due to communication delays, we still completed the essential components of Sprint 1. Although some deadlines were missed, the critical tasks were finished, and none of the work will require modifications later. This is thanks to proper requirements planning, which allowed us to fully understand the functionality of each component and mitigate future delays.

4.0 Relevant Links

<https://github.com/xLightless/uwe-enterprise-mlaas>
